


Task	Start Date	Finish Date	Comments
WP Splashpad Upgrade	03/04/2023	08/05/2023	<ul style="list-style-type: none"> New Splashpad wet pour Safety Surface will be laid w/c 24/04/2023 New Splashpad pump infrastructure commences w/c 08/05/2023
WP Crazy Golf Upgrade	20/03/2023	08/05/2023	<ul style="list-style-type: none"> All 7no golf holes reinstated w/e 21/04/2023 Grass carpet to be laid w/c 24/04/2023 3rd Bridge foundations laid and Bridge to be installed w/c 01/05/2023
WP Playground Equipment Upgrade	13/03/2023	28/04/2023	<ul style="list-style-type: none"> Sandpit fence has been dug out and works start w/c 24/04/2023 to reinstate the multi-play unit and associated chairs and tables. Other multi-play unit will have the minor repairs made w/c 24/04/23 and items back in action week commencing 01/05/23
WP Bank Water Feature	TBC	TBC	<ul style="list-style-type: none"> Scheme is being considered as part of WP Lake Safety Project compliance parameters as it is integral to Flood attenuation.

WP Splashpad Upgrade:



The existing wet pour has been lifted and the base ready for new wet-pour multi colour surface to be laid week commencing 24/04/2023 and will take 2 days (weather dependant)

WP Crazy Golf Upgrade:

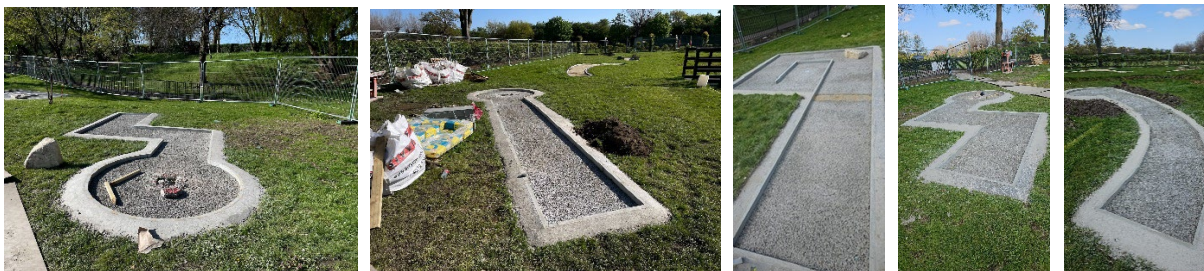

**OPENING SOON:
Wimbledon Park crazy golf**

The crazy golf course here in Wimbledon Park is getting a makeover. The newly refurbished course will open at the beginning of May 2023.

Stay up-to-date with all the latest council news. Visit Merton Council's social media channels, or sign up to the weekly *My Merton* e-news. merton.gov.uk/newsletter

All 7no NEW holes have been prepared grass carpet laid week commencing 24th April 2023. 3rd Bridge foundations have been set and bridge installed w/c 8th May.

WP Sandpit Upgrade



All the old framework has been dug out and new frame installations commenced w/c 17th April 2023. Idverde UK Team have now received all the replacement Seats, Tables and equipment for this area and the works will be complete by end of next week 28th April 2023
